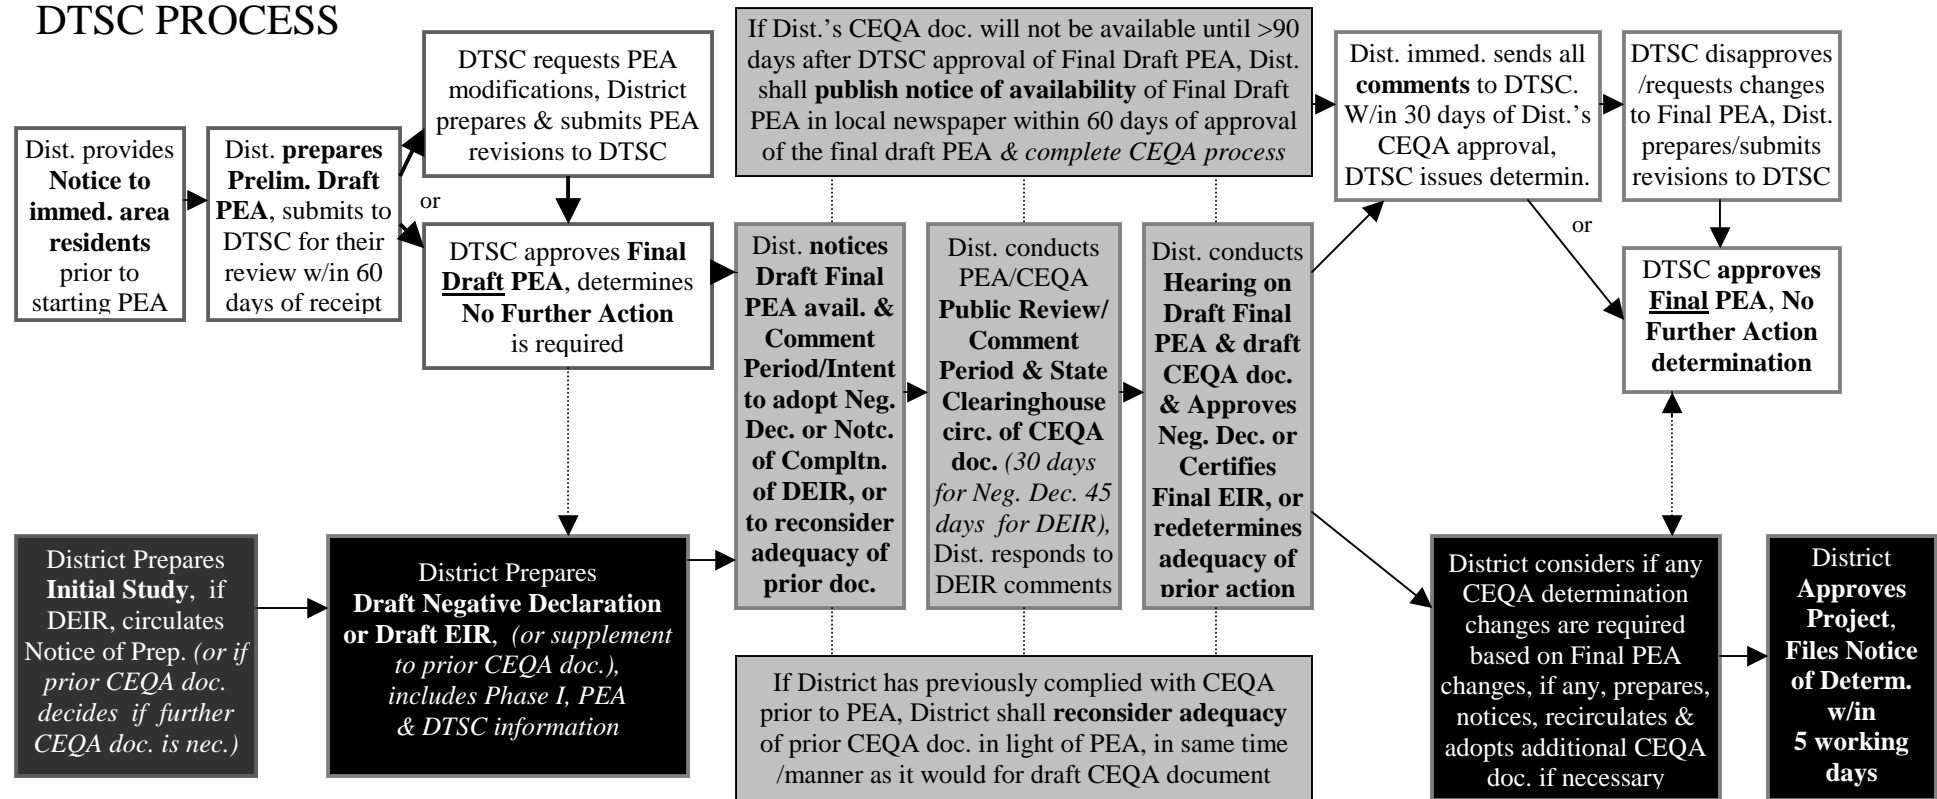# PEA / CEQA PUBLIC REVIEW / APPROVAL PROCESS
PROJECTS FOR WHICH <u>NO</u> RESPONSE ACTION IS REQUIRED

CONCURRENT ACTIONS

DTSC PROCESS

Dist. provides **Notice to immed. area residents** prior to starting PEA

Dist. **prepares Prelim. Draft PEA**, submits to DTSC for their review w/in 60 days of receipt

DTSC requests PEA modifications, District prepares & submits PEA revisions to DTSC

or

DTSC approves **Final Draft PEA**, determines **No Further Action** is required

If Dist.'s CEQA doc. will not be available until >90 days after DTSC approval of Final Draft PEA, Dist. shall **publish notice of availability** of Final Draft PEA in local newspaper within 60 days of approval of the final draft PEA & *complete CEQA process*

Dist. **notices Draft Final PEA avail. & Comment Period/Intent to adopt Neg. Dec. or Notc. of Compltn. of DEIR, or to reconsider adequacy of prior doc.**

Dist. conducts PEA/CEQA **Public Review/ Comment Period & State Clearinghouse circ. of CEQA doc.** *(30 days for Neg. Dec. 45 days for DEIR)*, Dist. responds to DEIR comments

Dist. conducts **Hearing on Draft Final PEA & draft CEQA doc. & Approves Neg. Dec. or Certifies Final EIR, or redetermines adequacy of prior action**

Dist. immed. sends all **comments** to DTSC. W/in 30 days of Dist.'s CEQA approval, DTSC issues determin.

DTSC disapproves /requests changes to Final PEA, Dist. prepares/submits revisions to DTSC

or

DTSC **approves Final PEA, No Further Action determination**

CEQA PROCESS

District Prepares **Initial Study**, if DEIR, circulates Notice of Prep. *(or if prior CEQA doc. decides if further CEQA doc. is nec.)*

District Prepares **Draft Negative Declaration or Draft EIR**, *(or supplement to prior CEQA doc.),* includes Phase I, PEA & DTSC information

If District has previously complied with CEQA prior to PEA, District shall **reconsider adequacy** of prior CEQA doc. in light of PEA, in same time /manner as it would for draft CEQA document

District considers if any CEQA determination changes are required based on Final PEA changes, if any, prepares, notices, recirculates & adopts additional CEQA doc. if necessary

District **Approves Project, Files Notice of Determ. w/in 5 working days**

Note that not all DTSC, CDE, CEQA or Education Code requirements or policies are shown on this chart and Districts may elect not to pursue a site at any time

CDE/SFPD interpretation of AB2644
2/28/01
